

The first terminal and the second sec

# STORM WATER POLLUTION PREVENTION PLAN

## A. PURPOSE:

The purpose of the Storm Water Pollution Prevention Plan (SWPPP) is to inform the Developer/Contractor of the following objectives they are required to meet:

- Prevent erosion where construction activities shall occur.
- Prevent pollutants from mixing with storm water.
- Prevent pollutants from being discharged by tropping them on—site, before they can offect the receiving waters.
- All regulations of Missauri Deportment of Natural Resources are met.
- All regulations of the Environmental Protection Agency are met.
- All regulations of the local municipality are met.

#### B. PROJECT DESCRIPTION:

The project is located in the Belleou Creek watershed in O'Fallon, Missouri. The project disturbs approximately 0.80 acres.

The project activities consist of the construction of one new building and parking lot. The site will be protected by the various erosion protection measures listed below:

- Siltation Control: The entire perimeter of the project that allows storm water to exit will have silt siltation control installed. Details of these devices are depicted on the detail plans prepared by Bax Engineering Cornpany, Inc.
- Revegetation: The site will consist of vorying ground slopes, upon completion of the grading activities the slope prone to erosion will be seeded and strawed to stabilize the slope and prevent erosion.

### C, MAINTENANCE AND INSPECTION:

Regular Maintenance: Weekly inspections of the project will include: (a) The repair of any sediment (silt) fence and/or staked straw bale borriers damaged or out of place; (b) The removal of any accumulated trash and/or debris; and (c) The remove of any externally deposited waste materials.

Periodic Inspections: Following each rain of more than 0.25 inch in 24 hours, the site will be inspected, and any necessary maintenance will be provided for a period of one year following the campletion of the above remediation measures. Summaries of the maintenance and the inspections will be maintained and shall be kept available from the owner. An inspection report shall be filed and kept on site for every inspection. The report shall detail the findings of the inspection and if any action was required. The inspection form needs to include, name of the site, name of the inspector, permit number, date of inspection, major observations and actions taken to correct problems and the signature of the inspector. The inspection reports need to be kept on file by the permittee for three years after the project is completed.

The field inspections will be conducted in a systematic manner to minimize the possibility of any significant feature being overlooked. A detailed checklist will be developed and followed for the examination. Particular ottention will be given to detecting evidence of erosion, slope instability, undue settlement, displacement, and tilting. Photographs and drawings will be used freely to record conditions in order to minimize descriptions. The field inspection will include appropriate features and items, including potential hazards to human life or property.

The condition of the slopes and vegetative cover will be evaluated and examined for erosion.


Measures will be taken to promote the growth of vegetation and repair of damoge caused by erosion and sedimentation. The inspection will also provide recommendations for measures that need to be undertaken immediately, based on the experience and judgment of the inspector. Necessary follow up inspections will be made as necessary to verify that any maintenance, alteration, or repair measures are accomplished by methods acceptable by standard engineering

Table 60-5 Soil Stabilization Schedule		
Soil Disturbance Activity or Condition	Required Stabilization Time	
Soil disturbance has ceased in areas greater than 2,000 square feet.	14 days	
After construction of dikes, swales, diversions, and other concentrated flow areas	5 days	
When slopes are steeper than 3 horizontal to 1 vertical	7 days	
When slopes are greater than 3% and longer than 150 feet.	14 days	
Perimeter controls around soil stockpiles.	End of workday	
Stabilization or covering of inactive stockpiles.	30 days	
When land disturbance is completed, permanent soil stabilization must be installed.	30 days	

# SPILL AND SITE POLLUTION:

Should an accidental spill occur refer to material safety dato sheets. Any spills of hazordous materials in quantities in excess of reportable quantities os defined by EPA or the state agency regulations, shall be immediately reported to the EPA National Response Center (800-424-8802) and Missouri Deportment of Natural Resources (573-634-2436). Reportable spills for petroleum products is greater than 50 gallons. All other reportable hozardous materials and their quantities may be found on the web site at http://www.dnr.mo.gov an the local number is 573-840-9750. Federal low requires the responsible party to report any release af oil if it reaches or threatens a sewer, lake, creek, stream, river, groundwater, wetlands, or area like a

An emergency spill kit is required to be onsite for all potential spills.

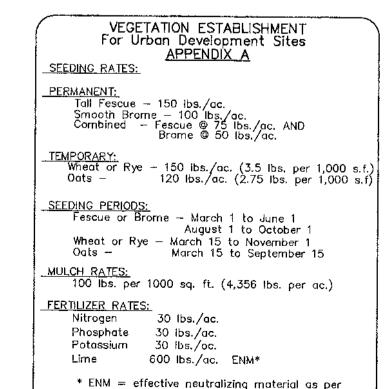

State evaluation of quarried rock.

BRYAN ROAD

BRYA

221 Point West Blvd. St. Charles, MO 63301 636-928-5552 FAX 928-1718



DISCLAIMER OF RESPONSIBILITY
I hereby specify that the documents intended to be authenticated by my seal are limited to this sheet, and I hereby disclaim any responsibility for all other Drawings, Specifications, Estimates, Reports or other documents or instruments relating to ar intended to be used for any part or parts of the architectural or engineering project or strivey.

CLIFFORD

HEITMANN

CLIFFORD

LIFFORD

LIFFORD

CLIFFORD

REVISIONS	
	PWSD2 comments
5-22-18	city & fire comments
	-

Veloper / Owner:
YAN ROAD ANIMAL HOSPITAL
I BRYAN ROAD
FALLON, MO 63366
6-272-3900

P+Z No. # 18-0

P-FZ No. # 18-000622 Approval Date: Mar. 1, 2018 City No. #

Page No.

9 of 17
