PIEPER ROAD IMPROVEMENTS

DETOUR

PHASE 5 — 95-067

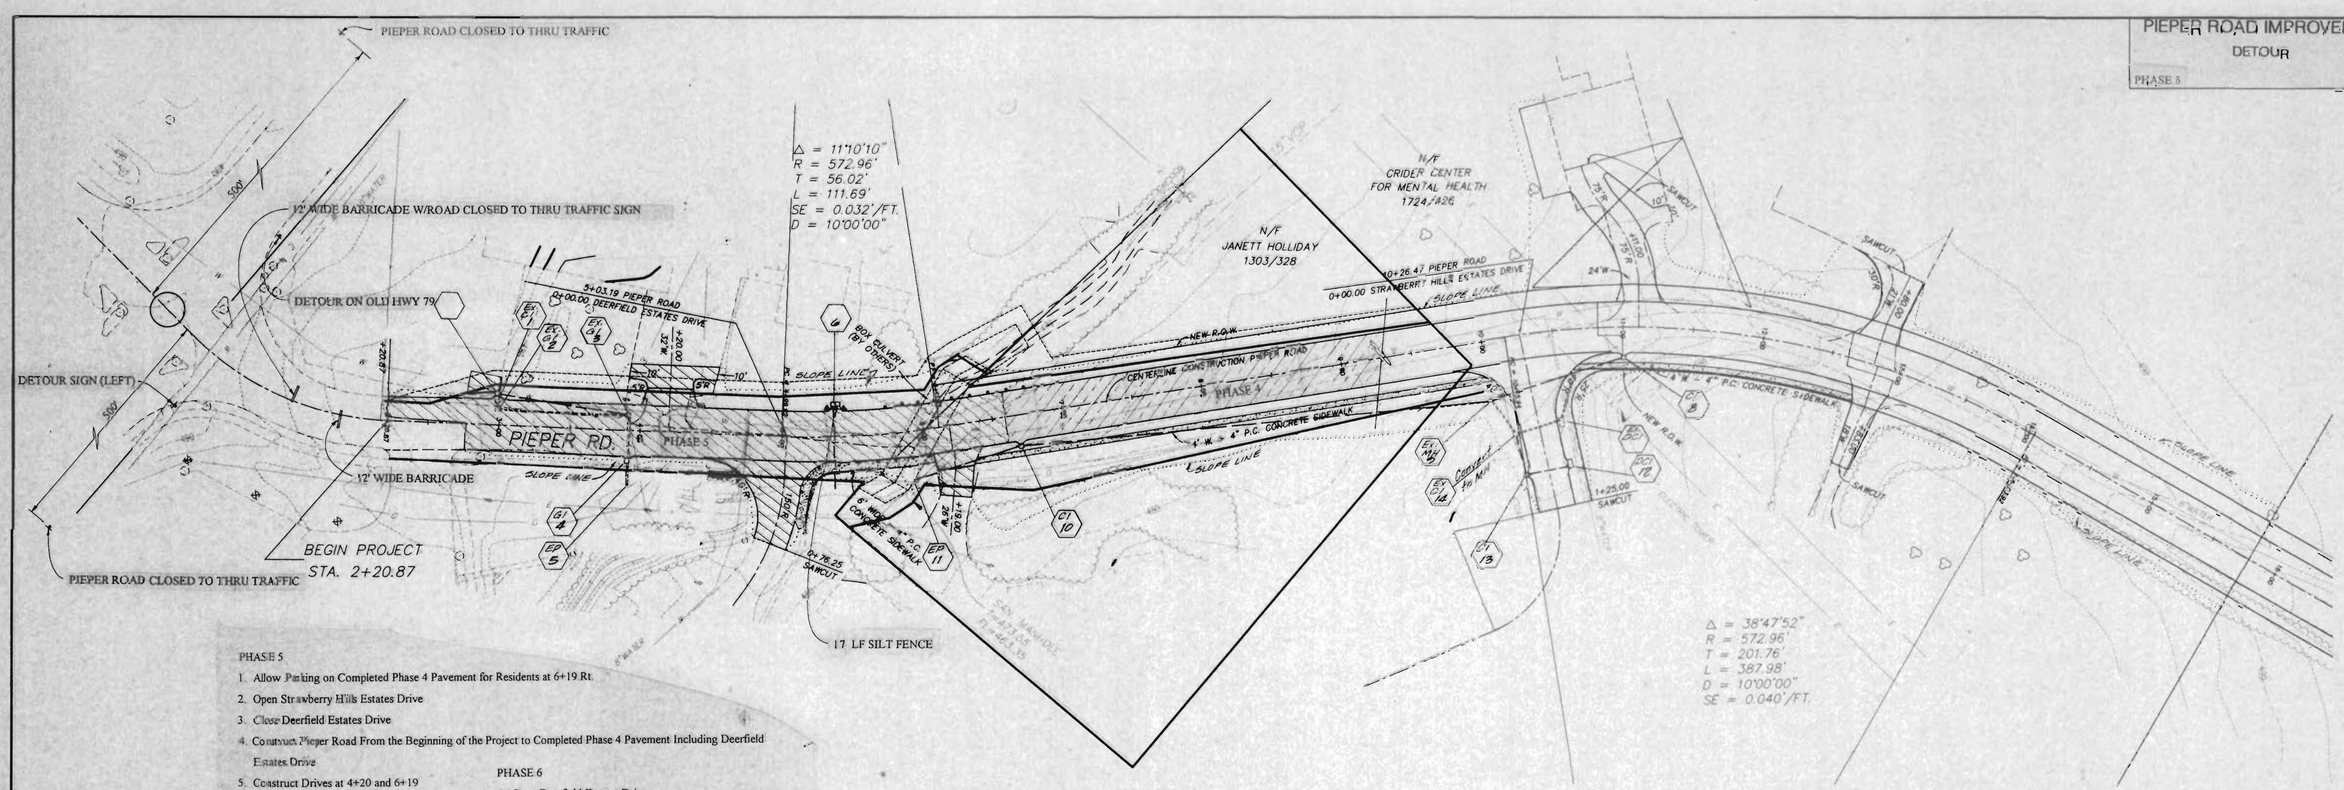

PHASE 5

1. Allow Parking on Completed Phase 4 Pavement for Residents at 6+19 Rt.
2. Open Strawberry Hills Estates Drive
3. Close Deerfield Estates Drive
4. Construct Pieper Road From the Beginning of the Project to Completed Phase 4 Pavement Including Deerfield Estates Drive
5. Construct Drives at 4+20 and 6+19

PHASE 6
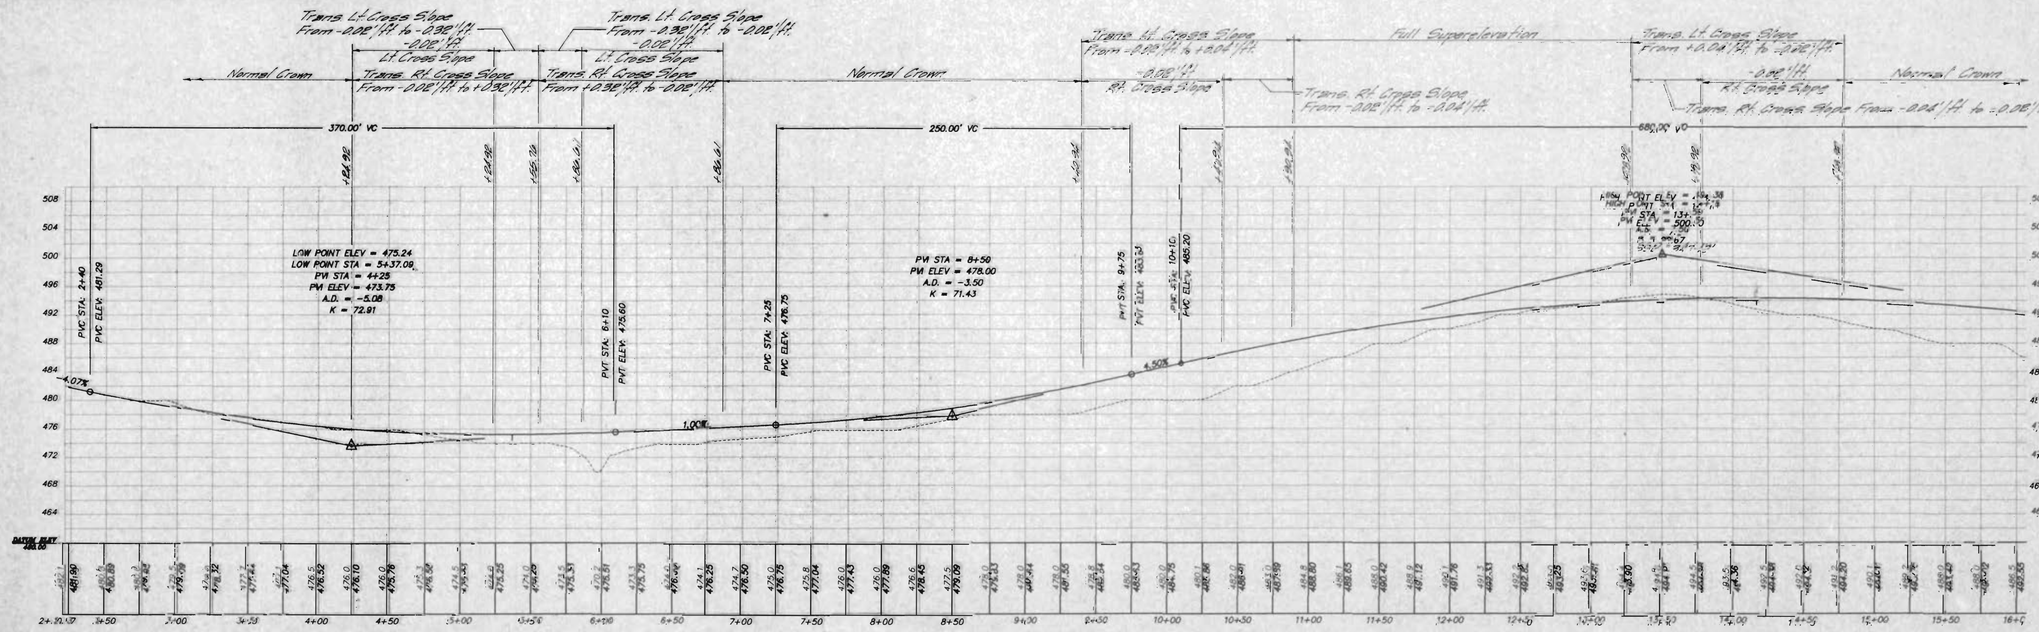
1. Open Deerfield Estates Drive
2. Install New and/or To Be Relocated Traffic Signs
3. Prepare New Pavement for Striping
4. Add New Pavement Markings and Striping
5. Open Pieper Road to Thru Traffic
6. Remove Detour Signs
